AI Project Intelligence & Risk Advisor

Project insights and evidence report

Workspace: AI Project Intelligence - fictional demo

Exported at (UTC): 14 Oct 2026, 06:27:38

Indexed source documents: 3

Purpose: project review, risk discussion and action planning using saved, evidence-grounded analysis.

Source-supported statements and derived health assessments are distinguished below. Missing information is not an all-clear. No new analysis is run during export.

Executive summary

Goal: help project reviewers turn uploaded documents into evidence-grounded scope, risk, delivery, blocker and action insights. [E18]

Overall health score: 42 / 100

Status: Needs attention

5 identified risks grouped by documented Risk ID; 2 additional observations. These are evidence records, not independently verified incidents.

Highest stated severity among rated records: R-02 Workspace data mixing (Critical) [E12] [E13] [E14]

Needs review: A new blocker B-03 was identified during export review preparation. [E19]

1 structured action records are available for review; this is not a verified open-task count.

Coverage is bounded by retrieved evidence. Partial results, missing ratings and unresolved conflicts must be reviewed against the sources. Full status, focus and limitations appear in the appendix.

Project overview

Coverage: partial. Findings are limited to available retrieved evidence.

Project goals

Goal: help project reviewers turn uploaded documents into evidence-grounded scope, risk, delivery, blocker and action insights. [E18]


Deliverables

Deliverables: one unified application with document upload, isolated workspaces, source retrieval, three project-analysis agents, Documentation Studio, Project Health, Project Assistant, an executive Overview and PDF/Word report export. [E20]

Risk Priority Matrix

Coverage: partial. Findings are limited to available retrieved evidence.

5 of 5 identified risks have comparable stated probability and impact ratings.

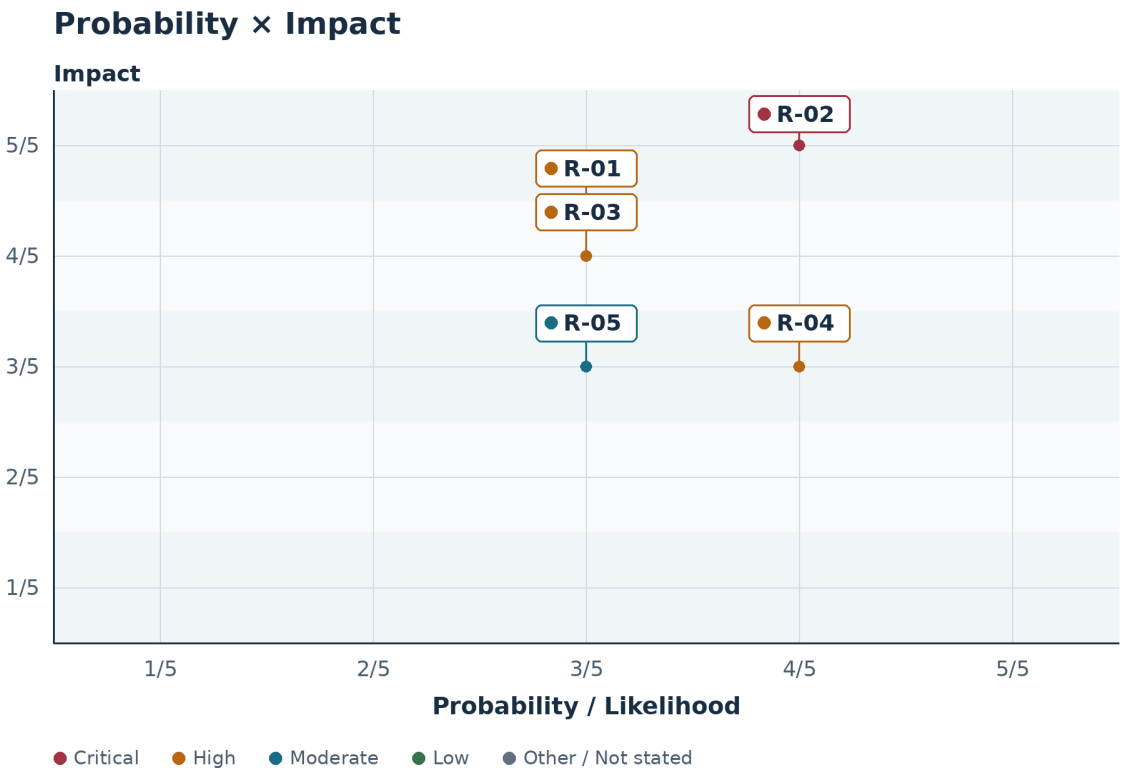

Leader lines retain exact source positions. Marker colour shows stated severity only.

Risk positions from stated source ratings. Full values and references follow in the register.

Positions use only stated values. Low / Moderate (Medium) / High are ordered categories; Critical impact is a separate category. Likely / Unlikely and Major / Minor use their own axes. n/5 ratings use a separate ordinal 1–5 scale, not percentages. Percentages use 0–100% axes. Mixed scales are shown separately.

Risk register

One row per documented Risk ID. Latest explicit dated snapshots are used only where chronology is unambiguous; all supporting snapshots remain cited. Severity is not calculated from chart position.

Risk ID and title	Probability / Impact	Severity / Status	Owner / Target date
R-05 Risk rating extraction	3/5 — Moderate 3/5 — Moderate	Moderate Open	Neha Rao 2026-10-13
R-03 Document format coverage	3/5 — Moderate 4/5 — High	High Open	Meera Shah 2026-10-10
R-01 RAG retrieval regression	3/5 — Moderate 4/5 — High	High In Progress	Neha Rao 2026-10-10
R-02 Workspace data mixing	4/5 — High 5/5 — Very High	Critical Open	Ravi Kumar 2026-10-09

Risk ID and title	Probability / Impact	Severity / Status	Owner / Target date
R-04 Stale incremental insights	4/5 — High 3/5 — Moderate	High In Progress	Arjun Das 2026-10-12

R-05 Risk rating extraction

Mitigation / documented action: Run T-11 labelled and natural-language rating checks [E3] [E4] [E5]

R-03 Document format coverage

Mitigation / documented action: Complete T-09 cross-format checks after T-17 provides approved fixtures [E6] [E7] [E8]

R-01 RAG retrieval regression

Mitigation / documented action: Run T-07 golden-source retrieval checks [E9] [E10] [E11]

R-02 Workspace data mixing

Mitigation / documented action: Complete T-08 isolation checks after T-16 provides isolated QA access [E12] [E13] [E14]

R-04 Stale incremental insights

Mitigation / documented action: Run T-10 incremental-upload race checks [E15] [E16] [E17]

Additional extracted observations

These observations have no unambiguous documented Risk ID and are not included in identified-risk counts.

Delivery forecast: the mentor demonstration target remains 2026-10-19; no revised delivery date is confirmed. [E1]

Blocker B-03: export font verification is blocked because the approved font checklist is unavailable; Action item: T-19 obtain the approved font checklist; Owner: Arjun Das; Due date: 2026-10-09; Status: Open; Linked risk: R-07; Recorded on: 2026-10-08. [E2]

Delivery outlook

Coverage: partial. Findings are limited to available retrieved evidence.

Delivery challenges

Blocker B-03: export font verification is blocked because the approved font checklist is unavailable; Action item: T-19 obtain the approved font checklist; Owner: Arjun Das; Due date: 2026-10-09; Status: Open; Linked risk: R-07; Recorded on: 2026-10-08. [E2]

Stated delivery outlook

Delivery forecast: the mentor demonstration target remains 2026-10-19; no revised delivery date is confirmed. [E1] [E21]

Blockers and action items

Coverage: partial. Findings are limited to available retrieved evidence.

Extracted issue or decision	Status	Owner / Due date	Evidence
A new blocker B-03 was identified during export review preparation.	Not stated	Not stated Not stated	[E19]

Documented actions

Action	Owner / Due date	Status / Dependency	Evidence
T-10 incremental upload race checks	Arjun Das 2026-10-12	Not stated Not stated	[E26]

Project health

Coverage: partial. Findings are limited to available retrieved evidence.

Overall health score: 42 / 100

Interpretation: Needs attention

Dimension	Score / Direction	Weight	State
Scope clarity	40 / 100 Higher = better	40%	assessed
Timeline risk	25 / 100 Higher timeline risk = more risk	35%	assessed
Blocker health	0 / 100 Higher = better	25%	assessed

Why this score

Overall = round half up(0.40 × scope clarity + 0.35 × (100 − timeline risk) + 0.25 × blocker health). All three dimensions must be assessable; weights are never silently redistributed. Bands: 75–100 fewer documented concerns; 45–74 review needed; 0–44 needs attention.

Scope clarity

Score: 40 / 100

Five scope categories receive 20 points when explicitly established, 10 when unclear, and 0 when not retrieved. No scope evidence makes this dimension unavailable.

20 + 20 + 0 + 0 + 0 = 40/100 [E18] [E20]

Scope category	Evidence state	Points	Evidence
Project goals	known	20.0	[E18]

Scope category	Evidence state	Points	Evidence
Deliverables	known	20.0	[E20]
Milestones	missing	0.0	Not stated
Timelines	missing	0.0	Not stated
Responsibilities	missing	0.0	Not stated

Timeline risk

Score: 25 / 100

Each unique schedule-risk or delivery-challenge statement adds risk points: critical 45, high 30, medium 20, low 10, unstated severity 25. Risk is capped at 100; a higher risk score is worse. Zero concerns requires an explicit source statement. Missing evidence never means no concerns. Conflicting zero and concern statements make the dimension unavailable.

min(100, 25) = 25 risk; health contribution = 100 − 25 = 75 [E2]

Blocker health

Score: 0 / 100

Each unique unresolved-issue or blocked-task statement reduces blocker health by 20 points. The count measures retrieved statements, not independently verified incidents. Zero concerns requires an explicit source statement. Missing evidence never means no concerns. Conflicting zero and concern statements make the dimension unavailable.

max(0, 100 − 20 × 5) = 0/100 [E23] [E18] [E24] [E25] [E19]

Methodology version: evidence-health-v1

Documentation and requirements

Coverage: partial. Findings are limited to available retrieved evidence.

User story 1: help project reviewers turn uploaded documents into evidence-grounded scope, risk, delivery…

Role / user: Not stated

Need / action: help project reviewers turn uploaded documents into evidence-grounded scope, risk, delivery, blocker and action insights

Benefit / value: Not stated

Acceptance criteria: Not stated

Information state: partial. [E18]

Evidence and appendix

Analysis provenance and limitations

Analysis	Freshness / Coverage	Generated at (UTC)
Scope	Current sources partial	14 Oct 2026, 06:19:18
Risk	Current sources partial	14 Oct 2026, 06:19:18
Blockers	Current sources partial	14 Oct 2026, 06:19:18
Documentation	Current sources partial	14 Oct 2026, 06:19:18
Health	Current sources partial	14 Oct 2026, 06:19:19
Briefing	Current sources partial	14 Oct 2026, 06:19:19
Briefing	Current sources partial	14 Oct 2026, 06:19:19

Briefing focus: Are we on track?

Briefing focus: What is blocking the project?

Missing means not established in this retrieved evidence, not necessarily absent from every document.

Local extractive mode uses fixed English-language rules; it is not a generative LLM and may miss indirect wording.

The evidence budget was reached. Narrow the analysis focus for more targeted coverage.

Delivery outlook is limited to explicit source statements. No delivery date or probability is predicted.

Assessment covers bounded retrieved evidence, not an exhaustive audit of every document or real-world project status.

Unknown fields are null in the API and shown as Not stated. No acceptance criteria, mitigation, or commitments are inferred.

User stories are structured drafts of explicit requirements, not newly invented requirements. Review partial stories before adoption.

Local mode uses conservative English extraction rules and may miss indirect wording.

The retrieval budget was reached. Use a narrower focus to review further evidence.

This is a transparent heuristic of retrieved project evidence, not a delivery probability, completion percentage, or independently verified assessment.

Repeated wording is deduplicated; differently worded statements about the same underlying problem may still be counted separately.

Dates are reported as written. No present-day lateness, revised deadline, or unstated severity is inferred.

A retrieval limit was reached; this assessment may omit additional evidence.

Source evidence

References identify the source file and recorded location. Quotations are preserved verbatim once per source location; historical snapshots are included when cited. Ellipses in main-section summaries indicate shortened text; consult the full quotation here.

[E1] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 17

Delivery forecast: the mentor demonstration target remains 2026-10-19; no revised delivery date is confirmed.

[E2] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 9

Blocker B-03: export font verification is blocked because the approved font checklist is unavailable; Action item: T-19 obtain the approved font checklist; Owner: Arjun Das; Due date: 2026-10-09; Status: Open; Linked risk: R-07; Recorded on: 2026-10-08.

[E3] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 32

Risk ID: R-05; Risk Title: Risk rating extraction; Risk Description: Delivery challenge involving risk rating extraction; Probability: 3/5 — Moderate; Impact: 3/5 — Moderate; Severity: Moderate; Status: Open; Owner: Neha Rao; Target Date: 2026-10-13; Due date: 2026-10-13; Mitigation: Run T-11 labelled and natural-language rating checks; Supporting Evidence: The matrix depends on retaining explicitly documented probability and impact fields; As of: 2026-10-08.

[E4] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 34

Risk ID: R-05; Risk Title: Risk rating extraction; Risk Description: Delivery challenge involving risk rating extraction; Probability: 3/5 — Moderate; Impact: 3/5 — Moderate; Severity: Moderate; Status: Open; Owner: Neha Rao; Target Date: 2026-10-13; Due date: 2026-10-13; Mitigation: Run T-11 labelled and natural-language rating checks; Supporting Evidence: The matrix depends on retaining explicitly documented probability and impact fields; As of: 2026-10-07.

[E5] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 35

Risk ID: R-05; Risk Title: Risk rating extraction; Risk Description: Delivery challenge involving risk rating extraction; Probability: 3/5 — Moderate; Impact: 3/5 — Moderate; Severity: Moderate; Status: Open; Owner: Neha Rao; Target Date: 2026-10-13; Due date: 2026-10-13; Mitigation: Run T-11 labelled and natural-language rating checks; Supporting Evidence: The matrix depends on retaining explicitly documented probability and impact fields; As of: 2026-10-05.

[E6] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 28

Risk ID: R-03; Risk Title: Document format coverage; Risk Description: Delivery challenge involving document format coverage; Probability: 3/5 — Moderate; Impact: 4/5 — High; Severity: High; Status: Open; Owner: Meera Shah; Target Date: 2026-10-10; Due date: 2026-10-10; Mitigation: Complete T-09 cross-format checks after T-17 provides approved fixtures; Supporting Evidence: Approved PDF and DOCX fixtures are required for cross-format verification; As of: 2026-10-08.

[E7] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 30

Risk ID: R-03; Risk Title: Document format coverage; Risk Description: Delivery challenge involving document format coverage; Probability: 3/5 — Moderate; Impact: 4/5 — High; Severity: High; Status: Open; Owner: Meera Shah; Target Date: 2026-10-10; Due date: 2026-10-10; Mitigation: Complete T-09 cross-format checks after T-17 provides approved fixtures; Supporting Evidence: Approved PDF and DOCX fixtures are required for cross-format verification; As of: 2026-10-07.

[E8] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 31

Risk ID: R-03; Risk Title: Document format coverage; Risk Description: Delivery challenge involving document format coverage; Probability: 3/5 — Moderate; Impact: 4/5 — High; Severity: High; Status: Open; Owner: Meera Shah; Target Date: 2026-10-10; Due date: 2026-10-10; Mitigation: Complete T-09 cross-format checks after T-17 provides approved fixtures; Supporting Evidence: Approved PDF and DOCX fixtures are required for cross-format verification; As of: 2026-10-05.

[E9] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 22

Risk ID: R-01; Risk Title: RAG retrieval regression; Risk Description: Delivery challenge involving rag retrieval regression; Probability: 3/5 — Moderate; Impact: 4/5 — High; Severity: High; Status: In Progress; Owner: Neha Rao; Target Date: 2026-10-10; Due date: 2026-10-10; Mitigation: Run T-07 golden-source retrieval checks; Supporting Evidence: Retrieval checks are needed to establish whether source passages support the answers; As of: 2026-10-08.

[E10] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 25

Risk ID: R-01; Risk Title: RAG retrieval regression; Risk Description: Delivery challenge involving rag retrieval regression; Probability: 3/5 — Moderate; Impact: 4/5 — High; Severity: High; Status: Open; Owner: Neha Rao; Target Date: 2026-10-10; Due date: 2026-10-10; Mitigation: Run T-07 golden-source retrieval checks; Supporting Evidence: Retrieval checks are needed to establish whether source passages support the answers; As of: 2026-10-05.

[E11] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 24

Risk ID: R-01; Risk Title: RAG retrieval regression; Risk Description: Delivery challenge involving rag retrieval regression; Probability: 3/5 — Moderate; Impact: 4/5 — High; Severity: High; Status: In Progress; Owner: Neha Rao; Target Date: 2026-10-10; Due date: 2026-10-10; Mitigation: Run T-07 golden-source retrieval checks; Supporting Evidence: Retrieval checks are needed to establish whether source passages support the answers; As of: 2026-10-07.

[E12] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 24

Risk ID: R-02; Risk Title: Workspace data mixing; Risk Description: Delivery challenge involving workspace data mixing; Probability: 4/5 — High; Impact: 5/5 — Very High; Severity: Critical; Status: Open; Owner: Ravi Kumar; Target Date: 2026-10-09; Due date: 2026-10-09; Mitigation: Complete T-08 isolation checks after T-16 provides isolated QA access; Supporting Evidence: Isolated QA access is required before workspace isolation can be verified; As of: 2026-10-08.

[E13] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 26

Risk ID: R-02; Risk Title: Workspace data mixing; Risk Description: Delivery challenge involving workspace data mixing; Probability: 4/5 — High; Impact: 5/5 — Very High; Severity: Critical; Status: Open; Owner: Ravi Kumar; Target Date: 2026-10-09; Due date: 2026-10-09; Mitigation: Complete T-08 isolation checks after T-16 provides isolated QA access; Supporting Evidence: Isolated QA access is required before workspace isolation can be verified; As of: 2026-10-07.

[E14] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 27

Risk ID: R-02; Risk Title: Workspace data mixing; Risk Description: Delivery challenge involving workspace data mixing; Probability: 4/5 — High; Impact: 5/5 — Very High; Severity: Critical; Status: Open; Owner: Ravi Kumar; Target Date: 2026-10-09; Due date: 2026-10-09; Mitigation: Complete T-08 isolation checks after T-16 provides isolated QA access; Supporting Evidence: Isolated QA access is required before workspace isolation can be verified; As of: 2026-10-05.

[E15] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 33

Risk ID: R-04; Risk Title: Stale incremental insights; Risk Description: Delivery challenge involving stale incremental insights; Probability: 4/5 — High; Impact: 3/5 — Moderate; Severity: High; Status: Open; Owner: Arjun Das; Target Date: 2026-10-12; Due date: 2026-10-12; Mitigation: Run T-10 incremental-upload race checks; Supporting Evidence: Incremental-upload checks must establish that refreshed results use the current source version; As of: 2026-10-05.

[E16] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 30

Risk ID: R-04; Risk Title: Stale incremental insights; Risk Description: Delivery challenge involving stale incremental insights; Probability: 4/5 — High; Impact: 3/5 — Moderate; Severity: High; Status: In Progress; Owner: Arjun Das; Target Date: 2026-10-12; Due date: 2026-10-12; Mitigation: Run T-10 incremental-upload race checks; Supporting Evidence: Incremental-upload checks must establish that refreshed results use the current source version; As of: 2026-10-08.

[E17] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 32

Risk ID: R-04; Risk Title: Stale incremental insights; Risk Description: Delivery challenge involving stale incremental insights; Probability: 4/5 — High; Impact: 3/5 — Moderate; Severity: High; Status: In Progress; Owner: Arjun Das; Target Date: 2026-10-12; Due date: 2026-10-12; Mitigation: Run T-10 incremental-upload race checks; Supporting Evidence: Incremental-upload checks must establish that refreshed results use the current source version; As of: 2026-10-07.

[E18] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 9

Goal: help project reviewers turn uploaded documents into evidence-grounded scope, risk, delivery, blocker and action insights.

[E19] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 7

A new blocker B-03 was identified during export review preparation.

[E20] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 10

Deliverables: one unified application with document upload, isolated workspaces, source retrieval, three project-analysis agents, Documentation Studio, Project Health, Project Assistant, an executive Overview and PDF/Word report export.

[E21] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 15

Delivery forecast: the mentor demonstration target remains 2026-10-19; no revised delivery date is confirmed.

[E22] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 11

Actions and pending decision

[E23] AI_Project_Meeting_Notes_02_Progress_and_Blockers_Corrected.docx | Paragraph/block 2

Progress review and blockers

[E24] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 12

Their earlier records remain unresolved.

[E25] AI_Project_Meeting_Notes_03_Export_Readiness_Update_Corrected.docx | Paragraph/block 8

New blocker

[E26] AI_Project_Meeting_Notes_01_Initial_Project_Review_Corrected.docx | Paragraph/block 16

Action item: T-10 incremental upload race checks; Owner: Arjun Das; Due date: 2026-10-12.
